

CHESS PROJECT RELEASE 1 BUILD AND TEST FORUM

ASX


6 February 2026



Acknowledging Country

ASX acknowledges the
Traditional Owners of
Country throughout
Australia. We pay
our respects to Elders
past and present.

Artwork by Lee Ann Hall
My Country My People



Housekeeping

Troubleshooting

- Please mute yourself when not speaking
- Please use the 'raise hand' feature on MS Teams if you would like to ask a question
- Please introduce yourself when talking for the benefit of all members
- Meeting is being recorded for the purposes of capturing decisions and actions
- Dial in details (audio only):
 - +61 2 7208 4607
 - Phone Conference ID: 350 525 873#
- Presentation materials were distributed before the meeting and will be published on the website.

Important Information

Competition Law Reminder

Workshop members are reminded to have regard to their obligations under competition law. In particular, please note that the Competition and Consumer Act prohibits a corporation from engaging with one or more persons in a concerted practice that has the purpose, effect or likely effect of substantially lessening competition.

Agenda

01 IDR2 AMO Acceptance Forum

02 Open Actions & Feedback

03 AMO Readiness & ITE Activity Update

04 AMO Legal Arrangements, Rule Change & Operational Procedures Update

05 Forward Engagement for 2026

01 IDR2 AMO Acceptance Forum

01 – IDR2 AMO Acceptance Forum

PLACEHOLDER TO BE PRESENTED ON THE DAY OF THE WORKING GROUP

The content of this slide is dependent on IDR2 AMO Readiness Tracker updates pending completion by AMOs

02 Open Actions & Feedback

02 - Open Actions

Actions as of 6 February 2026

#	Topic	Action	Raised	Due	Owner	Status
R1BT_8	Monday Rollback Test	ASX to work with AMOs to test Monday rollback post cutover	11 Sep 2025	Dec 2025	ASX	R1 Rollback tested 12 Dec 2025 - propose to close
R1BT_12	FIX Message Payload	ASX to review (AE) Tag 448 ASCII processing approach and validate if there are any considerations from a Regulatory Data perspective	11 Dec 2025	Jan 2026	ASX	Update to be provided during 6 Feb R1 B&T - propose to close
R1BT_13	AFII Documented Support	ASX to review AFII Pending Trade support alignment between AMO User Technical Documentation & Operational & Technical Standards, and AFII reference in AMO Attestation	11 Dec 2025	Jan 2026	ASX	Update to be provided during 6 Feb R1 B&T - propose to close
R1BT_14	AFII NFR for Pending Trades	ASX to confirm performance testing included Pending Trades via AFII	11 Dec 2025	Jan 2026	ASX	Update to be provided during 6 Feb R1 B&T - propose to close
R1BT_15	AMO Go-Live Attestation	AMOs to provide feedback on draft AMO Attestation by 16 January 2026	11 Dec 2025	Jan 2026	AMOs	Propose to close

03

AMO Readiness & ITE Activity Update

03 - AMO Industry Readiness Dashboard

As of 28 January 2026

AMO Operational Readiness

- All AMO Operational Readiness assessments complete

IDRs & Parallel Test

- Pre Parallel Test Cycle 2 commenced 28 Jan 2026
- Participating AMOs ready to commence IDR2 + Parallel Test Cycle 2 from 6 Feb 2026

Clearing Regression

- AMOs continuing to support Clearing Regression activities in their Customer Test Environments (specified securities)

Go-Live

- AMOs preparing to finalise all testing by end of February. Industry Test Environments to be taken offline so that CHESX changes for BAU can be performed by ASX.

Open AMO Readiness measures

AMO Readiness Metric	Qualitative or Quantitative	Impacted Milestone	Measure	On Track (Start measuring)	At Risk (if not completed)	Requires Remediation (if not completed)
AMO or Software Provider Readiness Self Assessment	Qualitative	Overall timeline	AMO or Software Provider to indicate how they are tracking	<i>AMO or Software Provider to indicate status as part of bilaterals</i>		
AMO Attestation	Quantitative	Go Live	Receipt of Attestation Form by specified dates	1 Feb 26	20 Feb 26	28 Feb 26

Completed AMO measures: (1) Functional Message Workflows, (2) Non-Functional and resilience testing, (3) Software Accreditation Completion, (4) AMO ITE Connectivity (5) AMO Operational Readiness (6) To-Be-Prod AMO Connectivity (7) AMO Parallel Test Deployment

AMOs	Milestone				
	Engagement	AMO Operational Readiness	IDRs	Parallel Test	Clearing Regression
AMO					

Note: AMOs not supporting Clearing Regression are reported as On Track to enable anonymised reporting.

03 - Known Issues Impacting AMOs


As of 6 February 2026

Ref ID	Issue Summary	Impacting	Scheduled Resolution
CHR-22126	AFII + FIX GW: (AR) & (AU) reject messages not generated when certain high-order ASCII characters are included in various fields	AMOs	Clearing Regression Patch 2
CHR-24704	Logout (5) not received when AMO sends Logon with an incorrect SenderCompID	AMOs	Clearing Regression Patch 2
CHR-24705	(Reopened) Logout (5) not always received when session terminated due to AMO HeartBtInt (108) value over 60 seconds	AMOs	Clearing Regression Patch 2
CHR-26942	Incorrect error message and pending trade behaviour when Trade Date is not a valid date	AMOs	Clearing Regression Patch 2
CHR-30691	Duplicate (AR)s generated (with the first being false) during Pod incident and restart	AMOs	Clearing Regression Patch 2
CHR-31372	Qty (Tag32) value getting padded out with extra decimal value zeros exceeding specified character length during ASX actions in the UI	AMOs	Clearing Regression Patch 2
New CHR-35113	Parallel Test Reconciliation Tool: Trade mismatch report False Positive breaks are reported when a corporate action diary adjustment occurs	AMOs	Clearing Regression Patch 2
New CHR-36534	AFII – Trade Cancellation rejected when original trade report is in earlier row in same input file but processing not yet complete	AMOs	Clearing Regression Patch 2

03 - ITE & To-Be-Prod planned availability timelines

AMOs to have tested AFII and (if enabled) Auxiliary Endpoint in To-Be-Prod by the end of Parallel Test Cycle 2

ITE

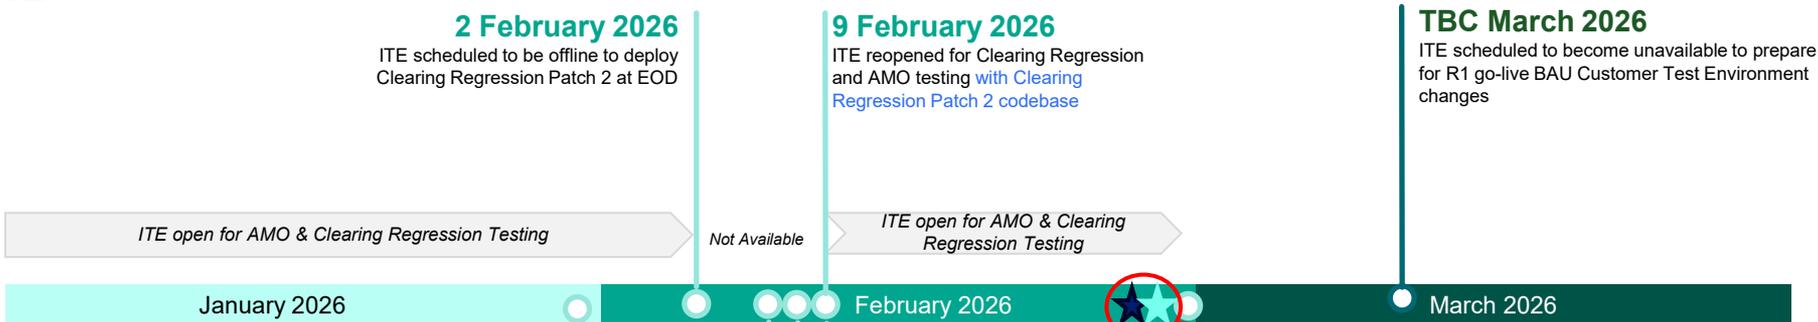

To-Be-Prod

28 January 2026

To-Be-Prod opened for Optional Pre Parallel Test Cycle 2 testing with Clearing Regression Patch 2 codebase

To-Be-Prod – Optional Pre Parallel Test Cycle 2

Not Available

5 February 2026

To-Be-Prod scheduled to be taken offline COB 5 Feb to prepare for IDR2

6 February 2026

IDR2 Commences (6-8 Feb)

9 February 2026

To-Be-Prod opens for first day of Parallel Test Cycle 2 (9-20 Feb)

To-Be-Prod – Parallel Test Cycle 2


To-Be-Prod – Post Parallel Test Cycle 2 optional extension

27 February 2026

To-Be-Prod may be extended further and will be dependent on discussions with AMOs.

AMO and CP Readiness attestations due by end of February 2026

03 - CHES Release 1 – Planned Upcoming AMO Activities

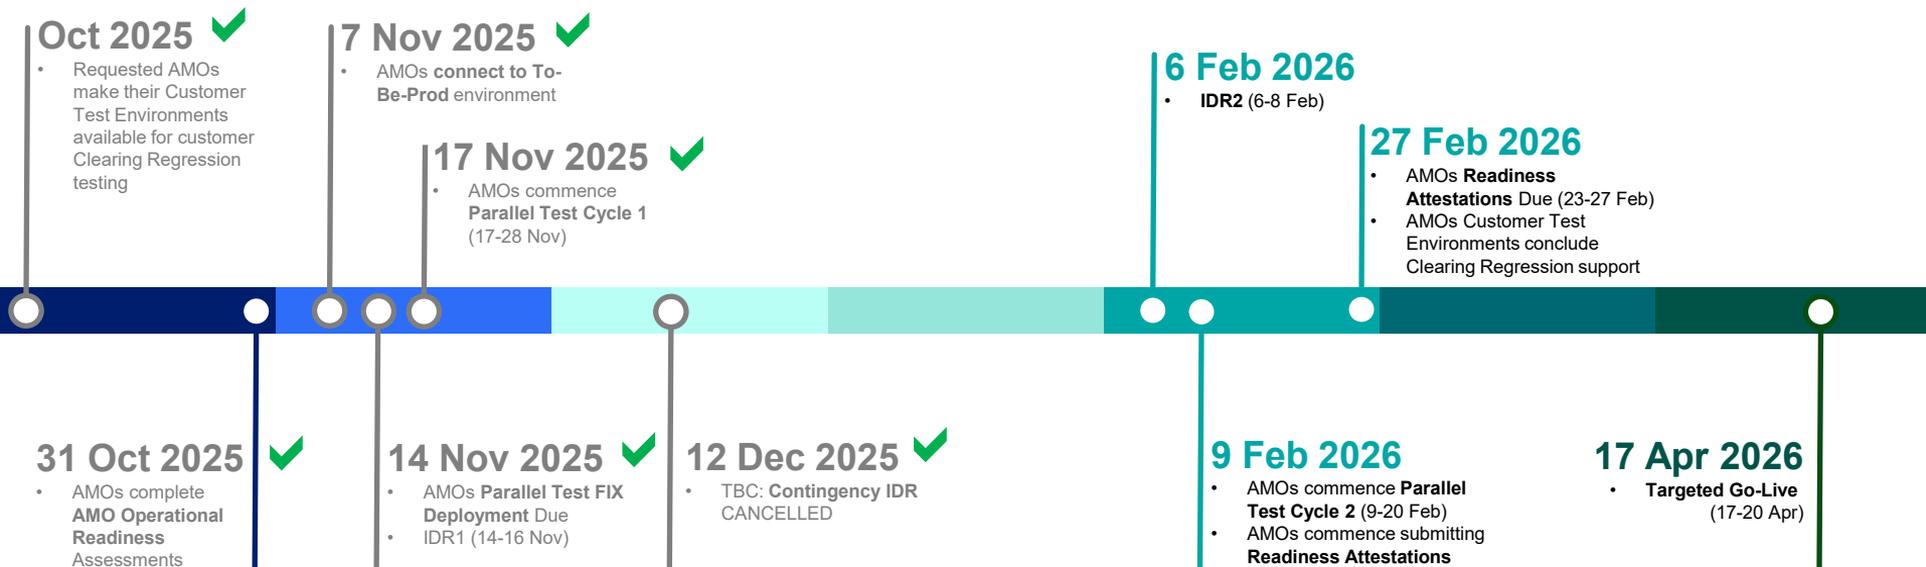

03 – AMO Attestation

Confirming AMO readiness for Release 1 Go-Live

- AMO Go-Live Readiness Attestation has been drafted and is planned to be distributed to AMOs by 9th February 2026
- AMOs requested to have authorised representative complete and submit go-live readiness attestations to ASX by 27 February 2026
- Completed AMO Go-Live Readiness Attestations to be emailed to CHESReplacement@asx.com.au



CHES Project External User Testing

AMO Release 1 Go-Live Readiness Attestation

This Readiness Attestation should be completed by a representative of the AMO with authority to complete agreements on the AMO's behalf and is accountable for the progress of the CHES Project within the organisation.

Representative Name	
Representative Job Title	
AMO Name (Full Organisation Name)	

The AMO confirms that:

- We have connected to the required CHES Release 1 test environments and have completed all functional and non-functional testing associated with our business-as-usual production workflows and processes
- Our testing includes transmission and receipt of trade and price messages through the following CHES Release 1 Trade Acceptance Service channels:
 - FIX Gateway
 - Alternate File Ingestion Interface (AFII) [select if applicable] As we have enabled the optional Auxiliary FIX Endpoint, our testing also includes transmission and receipt of trade and price messages through this channel
- We have verified our systems, including upstream or downstream systems if applicable, and our processes are both technically and operationally ready to transition to the CHES Release 1 Trade Acceptance Service in Production
- We will be ready when CHES Release 1 goes live and do not foresee any issues with our organisation continuing to operate business-as-usual activities in Production using the CHES Release 1 Trade Acceptance Service subject to the current proposed CHES milestones and the publicly available Go-Live dates

By signing the below, you certify you have authority to provide the attestation on behalf of your organisation.

Representative signature	Date
Representative Name and Job Title	

04

AMO Legal Arrangements, Rule Change & Operational Procedures Update

04 - Release 1 Consultation Timeline


ASX Clear Operating Rules and Procedures



Note: All dates are indicative and subject to change


04 - Release 1 Consultation Timeline

AMO Contractual Terms

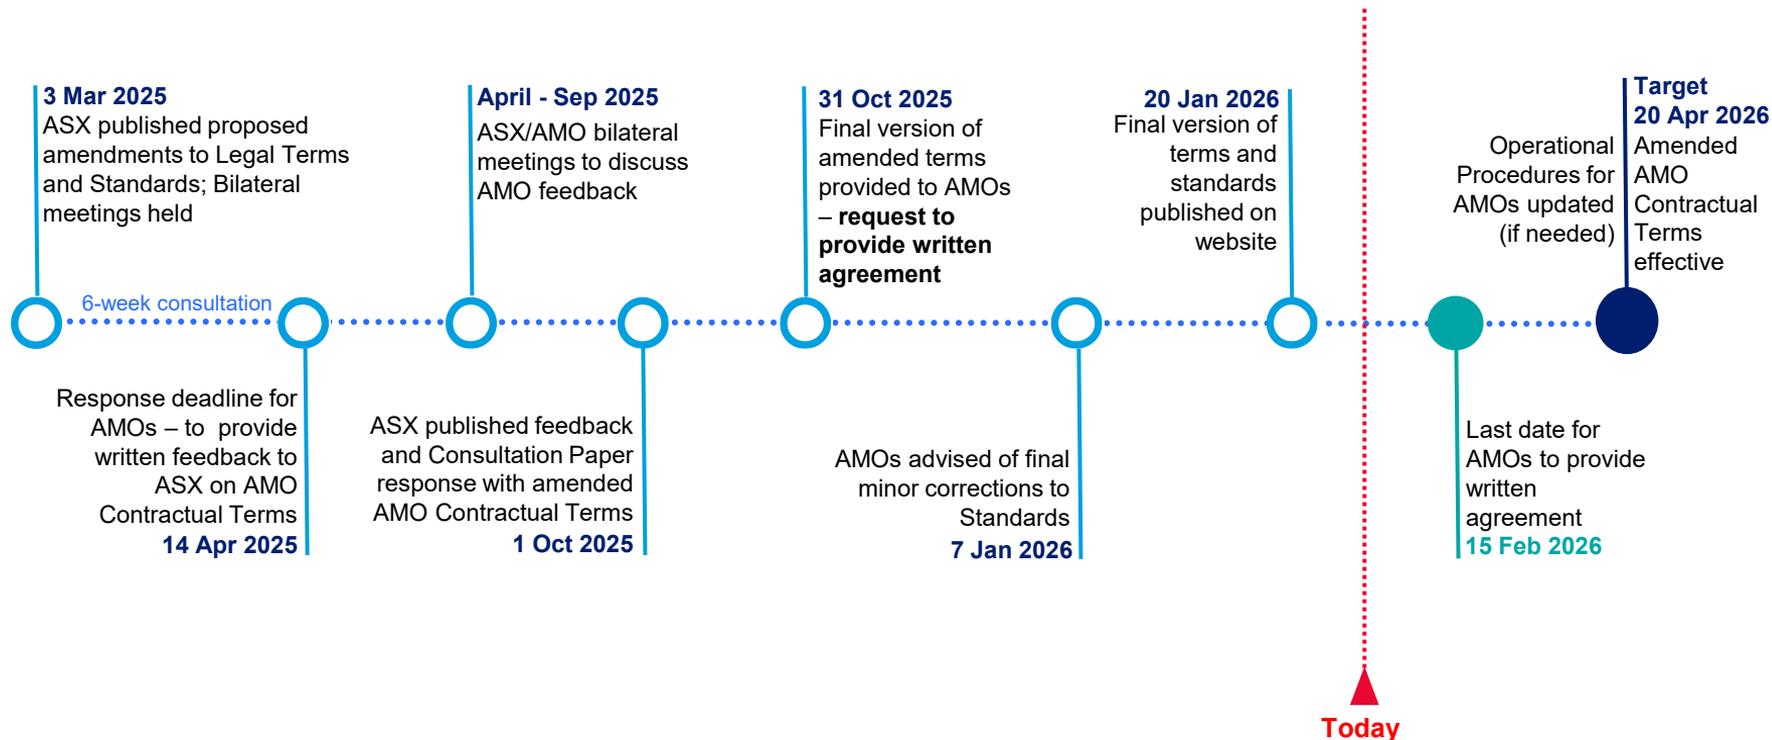

Note: All dates are indicative and subject to change

04 – AMO APGs and EIS Documents

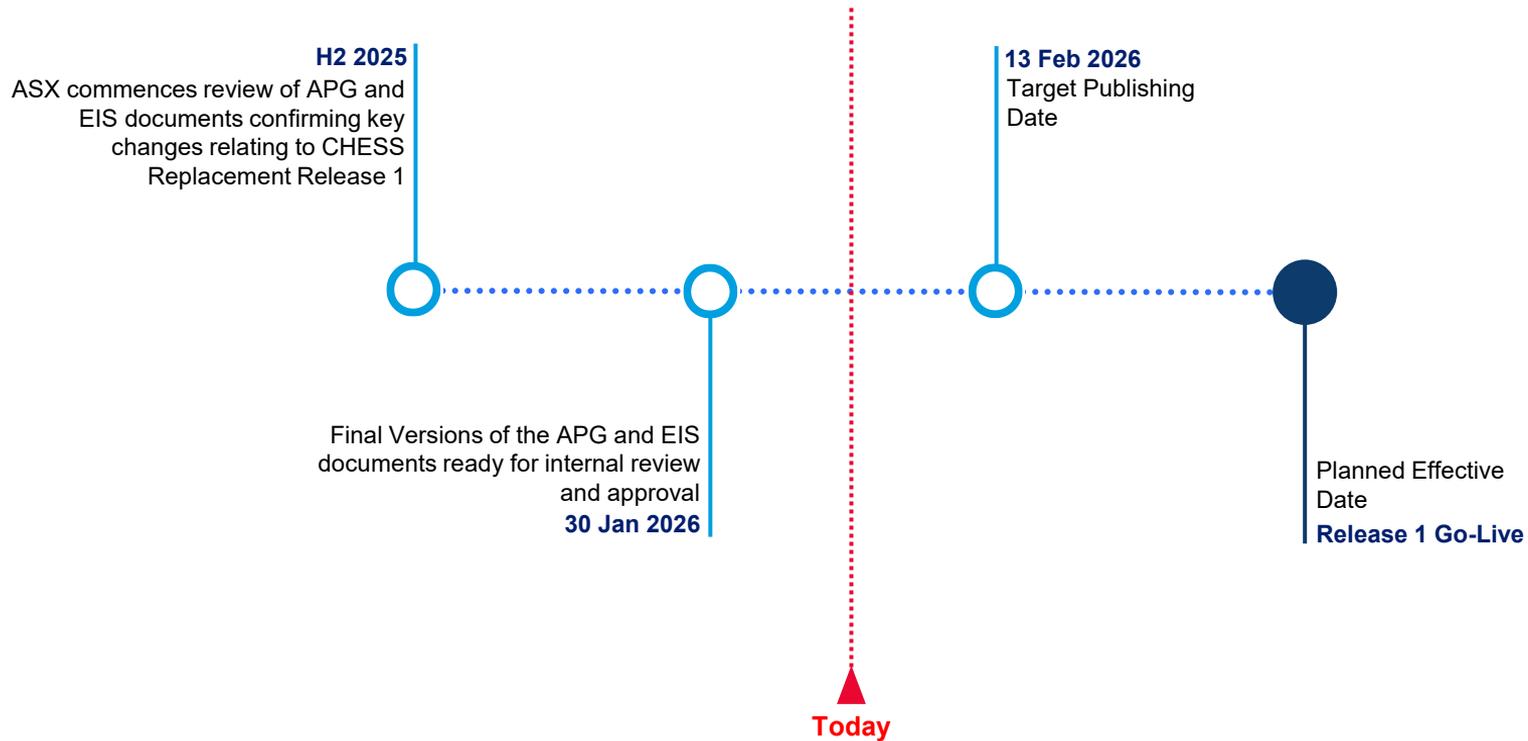

Note: All dates are indicative and subject to change

05 Forward Engagement for 2026

05 – Indicative Engagement Calendar: Rolling 3 Months


	January 2026	February 2026	March 2026
Technical Committee	No Technical Committee in January	5 February <ul style="list-style-type: none"> • CHES Release 1 Implementation • Preparation for the CHES Release 2 Industry Test Environment • Working Group Updates 	3 March <ul style="list-style-type: none"> • CHES Release 1 Implementation • CHES Release 2 Software Provider Build and Test Phase • Overview of CHES Release 2 Drop 3 UTDs • Working Group updates
Implementation & Transition Working Group	29 January <ul style="list-style-type: none"> • Release 1 Updates • Release 2 Timeline checkpoint update • Release 2 Connectivity and Test Kits 	26 February <ul style="list-style-type: none"> • Release 1 Updates • Release 1 Hypercare • Release 2 Updates 	26 March <ul style="list-style-type: none"> • Release 1 Go-live Readiness • Release 2 Updates
CHES Release 1 Build & Test Forum	No R1 Build and Test Forum in January	6 February <ul style="list-style-type: none"> • ITE Updates • IDR2 AMO Acceptance Forum • Go-Live Attestation 	19 March <ul style="list-style-type: none"> • Release 1 Go-Live Readiness
Business Design Working Group	No Business Design Working Group in January	4 February <ul style="list-style-type: none"> • Release 2 Drop 5 (Part 1 of 2) <ul style="list-style-type: none"> • Holding Adjustments • Corporate Actions Elections and Payment Channels 	4 March <ul style="list-style-type: none"> • Registries Focus Group
ISO Design Working Group	No ISO Design Working Group in January	25 February <ul style="list-style-type: none"> • Batch Settlement (Dec ISO overflow) • Holding Adjustments updates & changes • Elections Processing 	17 March <ul style="list-style-type: none"> • Drop 5 ISO Messages



Questions


Appendix

CHES Release 1 Indicative Pathway to Go-Live

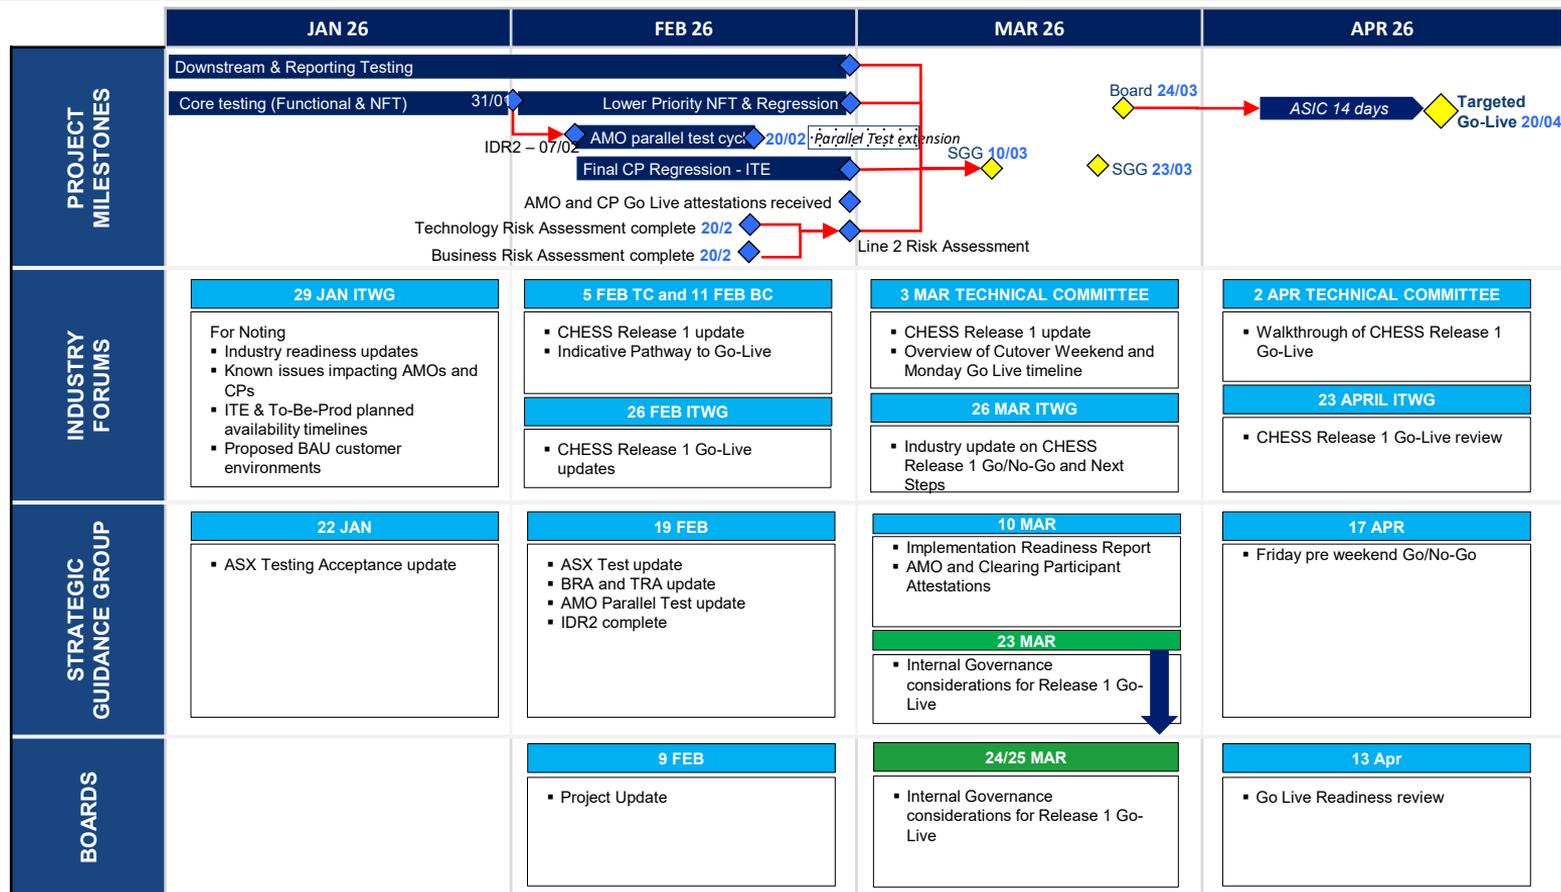


Indicative Industry Readiness Timeline

Following industry testing, AMO's and Clearing Participant's are expected to provide a Readiness Attestation prior to Management's decision to Go-Live.

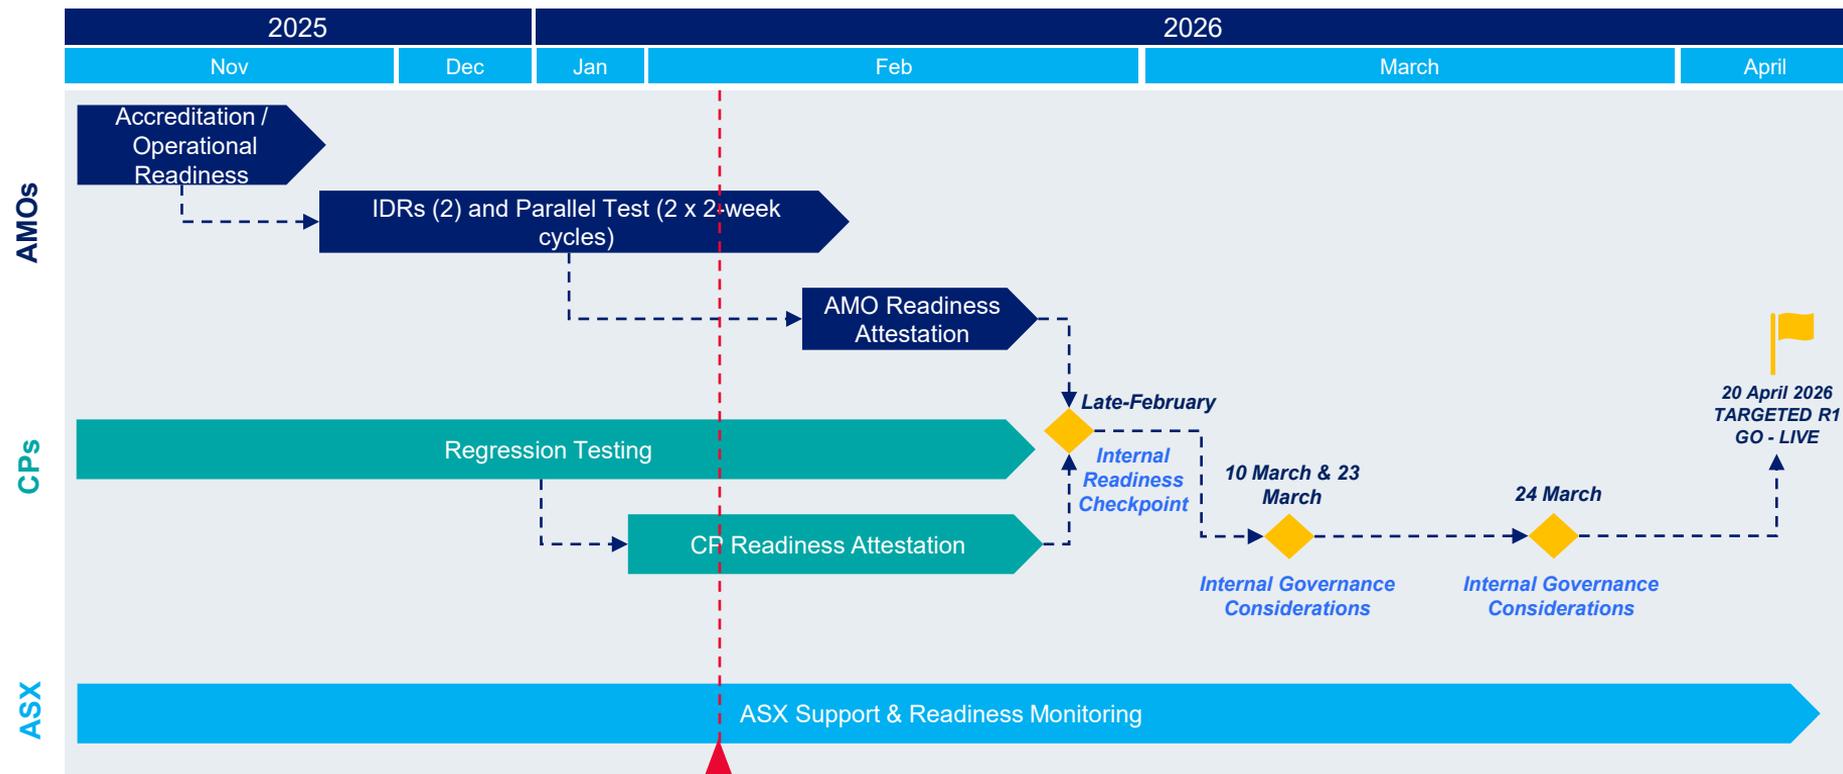

CHES Release 1 Indicative Project Timeline – Jan 2026

High level overview of the indicative timeline

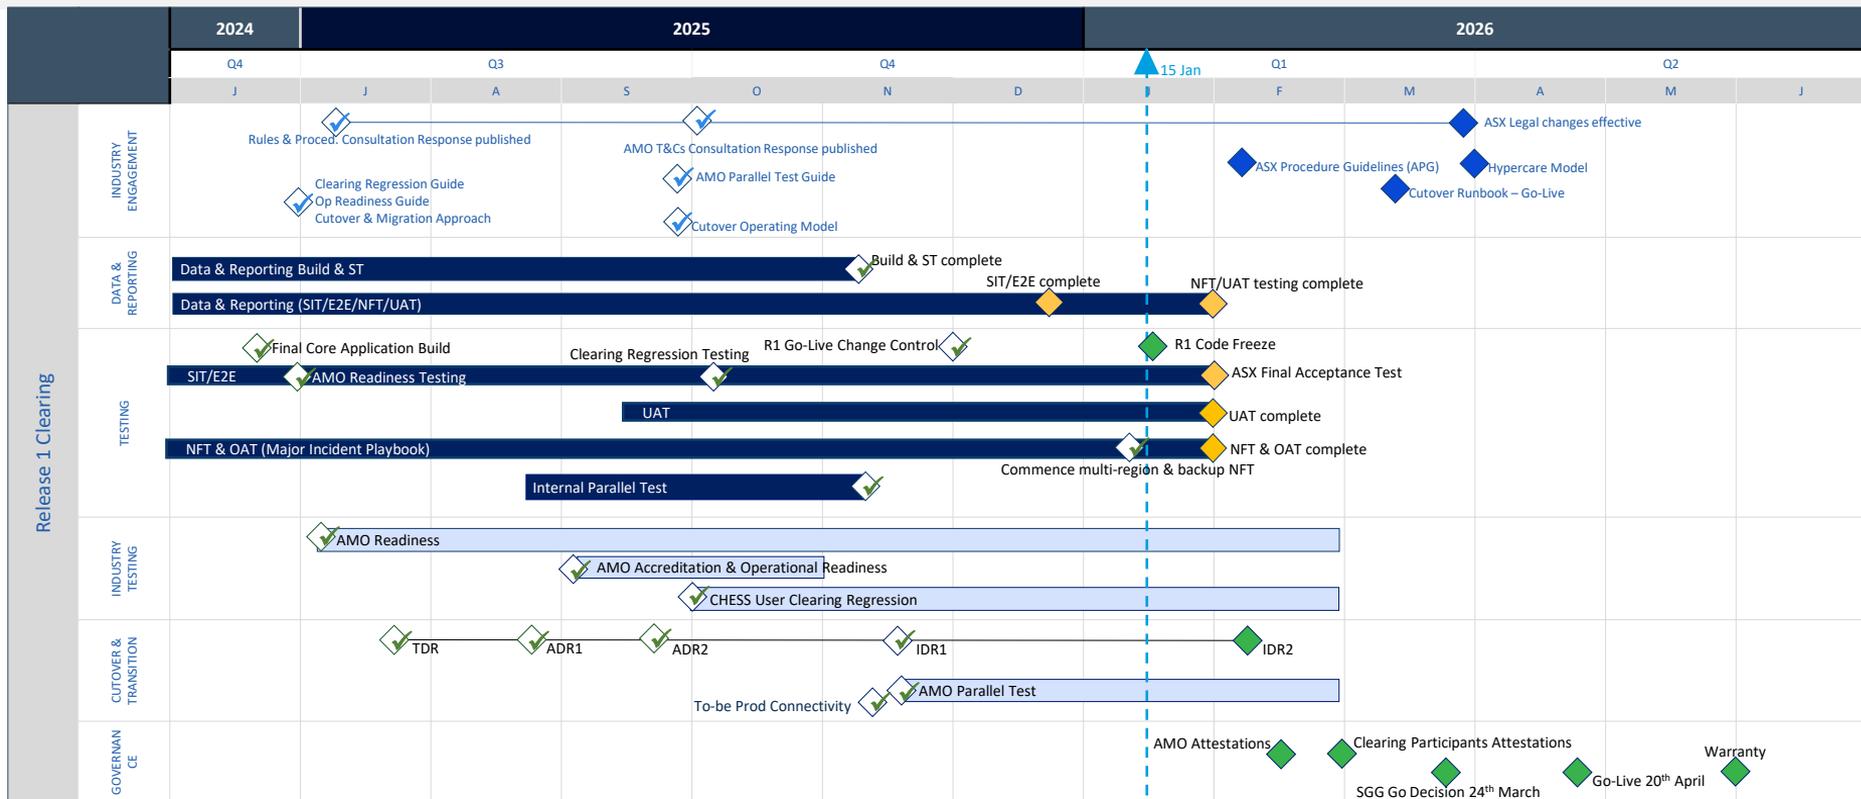

Upcoming Industry Test Phase Summary

All AMO Activity Required, Entry & Exit Criteria to be completed by AMOs or their Software Provider (where relevant), and dates are indicative and may be subject to change

	AMO Readiness	AMO Accreditation	AMO Operational Readiness	Clearing Regression	AMO Parallel Test
Planned Dates	Jul 2025 - Feb 2026	Sept – Early Nov 2025	Sept – Early Nov 2025	Oct 2025 – Feb 2026	Nov 2025 – Feb 2026
AMO Activity Required	Complete development of Drop 3 features, undertake testing, finalise software for accreditation (and ongoing testing to familiarise until Feb 2026)	Demonstrate software's ability to connect and interact with the CHES replacement system by completing specified accreditation scenarios	Demonstrate their organisation meets both the ASX's standards and operational requirements	AMOs revise participant IDs used in Trade Capture testing + support industry testing in their ITE integrated test environment	Reconcile current CHES production feed of trade registrations to CHES project feed on To-Be-Production infrastructure
Environment	R1 ITE	R1 ITE	R1 ITE	R1 ITE	R1 To-Be-Production
Entry Criteria	Completed build for features delivered in Drop 1 & 2 (ITE Open code base)	Successfully tested all AMO Accreditation scenarios and are ready to have AMO software assessed for formal Accreditation	Passed AMO Accreditation and have successfully tested all Operational Readiness scenarios.	Changes implemented to enable Clearing Participant testing in ITE, and processes required to support Clearing Participant testing in AMO ITE Integrated Test Environment communicated	Successfully completed AMO Operational Readiness assessment and ready to generate the FIX equivalent for Production trade registration and pricing data
Exit Criteria	Successfully tested all AMO Accreditation and are ready to have AMO software assessed for formal Accreditation	Demonstrated all AMO Accreditation scenarios have passed the success criteria	Demonstrated all Operational Readiness scenarios have passed the success criteria	AMO testing and Clearing Participant testing effectively coexisted enabling Clearing Participant attestations	Successful comparison of trade registration and pricing messages between current CHES and CHES project environments
Supporting Documentation	AMO User Technical Documentation	Release 1 AMO Accreditation Guide	Release 1 Guide to Operational Readiness Phase	Release 1 Guide to Operational Readiness Phase	Release 1 Guide to AMO Parallel Test
Supporting Documentation ETA	Feb 2025	Mar 2025	Jun 2025	Jun 2025	Sep 2025

Release 1 Engagement Activities: Completed

Activities and Documentation to Support R1 Industry Readiness

Activity	Subject	Purpose	Planned Date	Status
Publish Documentation	Release 1 Industry Test Approach	Documentation describing the detailed industry test approach and expected activities of each involved party, as well as timing, entry and exit criteria and expected test outcomes of all Release 1 industry test phases	Q3 2024	Published 6 Sep 2024
Publish Documentation	Release 1 FIX Specifications	Documentation providing a detailed specification of all FIX messages, including message structures, rules, and message flow diagrams. Market-relevant specifications will be published in iterations as ASX analyses and completes designs for each drop	Q4 2024	Published 14 Nov 2024
Publish Documentation	Release 1 Connectivity Guide	Documentation detailing the technical connectivity requirements to connect to the CHES replacement system, including connectivity method(s), network details and security details	Q4 2024	Published 17 Dec 2024
Engagement Activity	Release 1 ITE Open Overview	I&T WG session to provide overview of the opening of ITE, and discuss ASX proposed approach to tracking and reporting test phase activity	Q1 2025	Completed 27 Feb 2025
Publish Documentation	Release 1 AMO Build and Test Release Notes	Release Notes for the AMO Build and Test phase, including delivered functionality, FAQs and known issues in the environment	Q1 2025	Published 28 Feb 2025
Publish Documentation	Release 1 AMO Accreditation Guide	Documentation providing detail on the CHES replacement AMO Accreditation phase, expectations regarding conduct and expected results including the Accreditation process, connectivity, and message scenarios	Q1 2025	Published 31 March 2025
Engagement Activity	Release 1 Operational Readiness Overview	I&T WG session to provide overview & discuss the prerequisites & process for completing the Operational Readiness phase	Q2 2025	Completed 29 April 2025
Engagement Activity	Release 1 Clearing Regression Overview	I&T WG session to provide overview & discuss the prerequisites & process for completing the Clearing Regression phase	Q2 2025	Completed 29 April 2025 & 27 May 2025
Engagement Activity	Release 1 Cutover Overview	I&T WG session to provide overview & discuss the prerequisites & process for completing Release 1 cutover activities	Q2 2025	Completed 27 May 2025
Publish Documentation	Release 1 Guide to Operational Readiness Phase	Documentation detailing the Operational Readiness scenarios including mandatory success criteria	Q2 2025	Published 28 May 2025

Note: Indicative only, subject to change based on industry inputs and further planning.

Key |

Focus Groups

Documentation

Overviews

Checkpoints



Release 1 Engagement Activities: Completed

Activities and Documentation to Support R1 Industry Readiness

Activity	Subject	Purpose	Planned Date	Status
Publish Documentation	Release 1 Clearing Regression Test Guide	Documentation detailing the minimum ASX-specified Clearing Regression test scenarios, key activities and expectations regarding conduct and expected results including entry and exit criteria	Q2 2025	Published 25 Jun 2025
Publish Documentation	Release 1 Cutover Approach	Documentation detailing the cutover and migration approach, key activities, responsibilities including all verifications and validations required by ASX and the market, and milestones across the cutover and dress rehearsal windows	Q2 2025	Published 26 Jun 2025
Publish Documentation	Release 1 AMO Readiness Release Notes	Release Notes for the AMO Readiness phase, including delivered functionality, FAQs and known issues in the environment	Q2 2025	Published 02 Jul 2025
Engagement Activity	AMO IDR & AMO Parallel Phase Overview	I&T WG session to provide overview & discuss the prerequisites & process for completing the IDR & AMO Parallel Test phase	Q3 2025	Completed 29 Jul 2025
Publish Documentation	Release 1 Guide to AMO Parallel Test	Documentation providing detail on the AMO Parallel Test phase, key activities and expectations and expected results including entry and exit criteria	Q3 2025	Published 29 Sep 2025
Publish Documentation	R1 Cutover Operating Model	Documentation providing AMOs with key cutover tasks and milestones, with an outline of detailed steps including planned timing.	Q3 2025	Published 26 Sep 2025
Publish Documentation	R1 Cutover Runbook	The R1 Cutover Runbook will be used in dress rehearsals and refined as required ahead of the final go-live event. Note that the cutover runbook will also include the steps required to rollback	Q4 2025	Published 31 Oct 2025
Publish Documentation	Release 1 Clearing Regression Release Notes	Release Notes for the Clearing Regression phase, including delivered functionality, FAQs and known issues in the environment	Q4 2025	Published 7 Oct 2025
Publish Documentation	Release 1 AMO Implementation Dress Rehearsal Release Notes	Release Notes for the AMO IDR phase, including AMO Parallel Test, delivered functionality, FAQs and known issues in the environment	Q4 2025	Published 14 Nov 2025

Note: Indicative only, subject to change based on industry inputs and further planning.

Key |

Focus Groups

Documentation

Overviews

Checkpoints

ASX

Closed Actions (1 of 2)

#	Topic	Action	Raised	Closed	Owner	Status
R1BT_1	Testing Scenarios	AMOs to provide input as to the failover / DR scenarios they would like covered in the testing plan	15 Aug 2024	18 Mar 2025	AMOs	Closed
R1BT_2	FIX Messaging	ASX to provide iterative updates on FIX specification document to AMOs AMOs to provide feedback on FIX messaging specifications	28 May 2024	18 Mar 2025	AMOs & ASX	Closed
R1BT_3	Condition Codes & BoQ	AMOs to provide feedback on required Condition Codes & BoQ for AMO Readiness deployment	14 May 2025	12 Jun 2025	AMOs	Closed
R1BT_4	Unique Trade Identifier	ASX & AMOs to bilaterally review and agree method to ensure TradeID is unique across all AMOs and all times	14 May 2025	12 Jun 2025	ASX & AMOs	Closed
R1BT_5	Clearing Regression	ASX & AMOs to bilaterally discuss ASX questions related to AMOs ability to support TP/CP integrated testing during Clearing Regression	14 May 2025	12 Jun 2025	ASX & AMOs	Closed
R1BT_6	Release 1 Go-Live Date	AMOs to review ability to support Release 1 Go-Live date	14 May 2025	12 Jun 2025	AMOs	Closed

Closed Actions (2 of 2)

#	Topic	Action	Raised	Closed	Owner	Status
R1BT_7	Cutover – Comms Approach	ASX to perform PoC on proposed MS Teams channel communications approach during cutover	12 Jun 2025	16 Oct 2025	ASX	Closed
R1BT_9	Logout 5 Message Frequency	ASX to communicate changes to Logout 5 frequency	16 Oct 2025	13 Nov 2025	ASX	Closed
R1BT_10	To-Be Production Connectivity Timeline	ASX to update Amber at risk date for to-be production AMO connectivity from 24 Oct to 31 Oct 2025	16 Oct 2025	13 Nov 2025	ASX	Closed
R1BT_11	AMO run sheet steps for Cutover	AMOs to provide run sheet steps for Release 1 Cutover	16 Oct 2025	13 Nov 2025	AMOs	Closed

Disclaimer / Important Information

Information provided in this presentation is for educational purposes and does not constitute financial product advice.

You should obtain independent advice from an Australian financial services licensee before making any financial decisions. Although ASX Limited ABN 98 008 624 691 and its related bodies corporate (“ASX”) has made every effort to ensure the accuracy of the information as at the date of publication, ASX does not give any warranty or representation as to the accuracy, reliability or completeness of the information.

To the extent permitted by law, ASX and its employees, officers and contractors shall not be liable for any loss or damage arising in any way (including by way of negligence) from or in connection with any information provided or omitted or from anyone acting or refraining to act in reliance on this information.

Past performance of the ASX sharemarket and of any financial products referenced in this presentation is not a reliable indicator of future performance.

© Copyright 2026 ASX Operations Pty Limited ABN 42 004 523 782. All rights reserved 2026.



Thank you

ASX

This document provides general information only and may be subject to change at any time without notice. ASX Limited (ABN 98 008 624 691) and its related bodies corporate ("ASX") makes no representation or warranty with respect to the accuracy, reliability or completeness of the information. To the extent permitted by law, ASX and its employees, officers and contractors shall not be liable for any loss or damage arising in any way (including by way of negligence) from or in connection with any information provided or omitted, or from anyone acting or refraining to act in reliance on this information.

© Copyright ASX Operations Pty Limited ABN 42 004 523 782. All rights reserved 2026.
